Recorded: 4/17/2025 at 10:24:49.0 AM

County Recording Fee: lowa E-Filing Fee: \$0.00

Combined Fee: Revenue Tax: \$0.00 Delaware County, Iowa Daneen Schindler RECORDER

BK: 2025 PG: 953

REAL ESTATE TRANSFER - GROUNDWATER HAZARD STATEMENT

TO BE COMPLETED BY TRANSFEROR

TRANSF	EROR:			
Name	Allen W. Detweiler and Sarah R. Detweiler			
Address	2834 285th Street	Hopkinton	IA	52237
	Number and Street or RR	City, Town or PO	State	Zip
TRANSF	EREE:			
Name	Herman Stutzman and Edna Stutzman			
Address	2502 220th Ave	Dehli	IA	52223
	Number and Street or RR	City, Town or PO	State	Zip
Address	of Property Transferred:			
2834 285	5th Street, Hopkinton, IA 52237			
Number a	nd Street or RR	City, Town or PO	State	Zip
Legal De	escription of Property: (Attach if necessary)			
Parcel 20	21-61, Part of 2017-04 In SW-SW, 6-87N-3W,	Delaware County, according to plat re	corded in Book 2021	, Page 1862
2. Solid X	(check one) There are no known wells situated on this proper forth on an attached separate sheet, as nece Waste Disposal (check one) There is no known solid waste disposal site of there is a solid waste disposal site on this proper attached to this document. dous Wastes (check one)	erty. The type(s), location(s) and legal s ssary. n this property. operty and information related thereto		
4. Under	There is no known hazardous waste on this p There is hazardous waste on this property an this document. rground Storage Tanks (check one) There are no known underground storage tan motor fuel tanks, most heating oil tanks, ciste There is an underground storage tank on this	nd information related thereto is provid nks on this property. (Note exclusions e erns and septic tanks, in instructions.)	such as small farm ar	nd residential
<u>ا</u>	are listed below or on an attached separate s		Kilowii substalice(s)	containeu

5. Private Burial Site (check one)
There are no known private burial sites on this property.
There is a private burial site on this property. The location(s) of the site(s) and known identifying information of the
decedent(s) is stated below or on an attached separate sheet, as necessary.
6. Private Sewage Disposal System (check one)
All buildings on this property are served by a public or semi-public sewage disposal system.
This transaction does not involve the transfer of any building which has or is required by law to have a sewage
disposal system.
There is a building served by private sewage disposal system on this property or a building without any lawful sewage disposal system. A certified inspector's report is attached which documents the condition of the private sewage disposal system and whether any modifications are required to conform to standards adopted by the Department of Natural Resources. A certified inspection report must be accompanied by this form when recording. There is a building served by private sewage disposal system on this property. Weather or other temporary physical conditions prevent the certified inspection of the private sewage disposal system from being conducted. The buyer has executed a binding acknowledgment with the county board of health to conduct a certified inspection of the private sewage disposal system at the earliest practicable time and to be responsible for any required modifications to the private sewage disposal system as identified by the certified inspection. A copy of the binding acknowledgment is attached to this form. There is a building served by private sewage disposal system on this property. The buyer has executed a binding acknowledgment with the county board of health to install a new private sewage disposal system on this form. There is a building served by private sewage disposal system on this property. The building to which the sewage disposal system is connected will be demolished without being occupied. The buyer has executed a binding acknowledgment with the county board of health to demolish the building within an agreed upon time period. A
copy of the binding acknowledgment is provided with this form. [Exemption #9]
☐ This property is exempt from the private sewage disposal inspection requirements pursuant to the following
Exemption [Note: for exemption #9 use prior check box]:
The private sewage disposal system has been installed within the past two years pursuant to permit number
Information required by statements checked above should be provided here or on separate sheets attached hereto:
Well is located approximately 25 feet straight North from the house
Wen's located approximately 25 feet straight worth month the mouse
I HEREBY DECLARE THAT I HAVE REVIEWED THE INSTRUCTIONS FOR THIS FORM AND THAT THE INFORMATION STATED
ABOVE IS TRUE AND CORRECT.
(1501
921) -785-7N-1
Signature: Telephone No.: 700 / 000
(Transferor or Agent)



GOVERNOR KIM REYNOLDS LT. GOVERNOR CHRIS COURNOYER

DIRECTOR KAYLA LYON

TIME OF TRANSFER INSPECTION TOT# 14677 ROGER GROTH CERT # 8813

-Site Information-

Parcel Description: 410060001000

Address: 2834 285th St., Hopkinton, IA 52237 County: Delaware

Owner Information

Property is owned by a business: No

Business Name:

Owner Name: Allen & Sarah Detweiler Email Address: jfass@knightbarry.com

Address: 2834 285th St, Hopkinton, IA 52237

Phone No: 563-608-0178

-Site related information-

No Of Bedrooms: 4

Facility Type: Residential

Last Occupied:

Permit issued by County: Yes

All plumbing fixtures enter septic system: Yes

Property Information Comments:

Inspection Date: 04/08/2025

Currently Occupied: Yes

System Installation Date: 05/15/2017

Permit Number: 2613

County contacted for records: Yes

Primary Treatment

Tank 1 Septic tank

Tank Name: Tank 1 Septic tank Type: Septic Tank Tank Size (Gal): 1,250

Tank Material: Concrete Tank Corrosion Type: None Liquid Level Type: Above Baffle

No. of Compartments: 2 Pump Tank Chamber: No Licensed Pumper Name: Groth Services

LLC

Date Pumped: 4/8/2025 Meets Setback to Well: Yes Well Type: Private

Distance To Well (Ft.): >100' Is Accessible: Yes Lid Intact: Yes

Risers Intact: Yes

Effluent Filter Present: Yes

Watertight: Yes

Tank/Vault Pumped: Yes

Inlet Baffle Present: Yes

Outlet Baffle Present: Yes

Functioning as Designed: Yes

Tank Comments: Septic tank was overfull because the effluent filter was completely plugged. Also, the outlet line is exiting the tank at a very steep angle which raises the invert for outflow. This will be repaired next week by Groth Services.

General Primary Treatment Comments:

Distribution Type

Distribution Box 1

Label: Distribution Box 1

Material Type: Plastic

Accessible: No

Box Opened: Yes

Baffle Present: No

Speed Levelers Present: No

Watertight: Yes

Functioning As Designed: Yes

General Distribution System Comments:

Secondary Treatment

Lateral Field1

Distribution Type: **Distribution Box**

Lines: 2

Gallons Loaded: 300.

Distance To Well (Ft.): >100'

Grass Cover Present: No

Easement Present: N/A

Material Type: Rock and PVC Pipe

Total Length of Absorption Line: 200

Meets Setback to Well: Yes

Lateral Lines Probed: Yes

Lateral Lines Equal Length: Yes

Functioning as Designed: Yes

Trench Width: 36

System Hydraulic Loaded: Yes

Well Type: Private

Saturation or Ponding Present: No

System Located on Owner Property: Yes

Comments: Lateral field is very small for a four-bedroom home. There is a vegetable garden over most of the soil absorption system.

General Secondary Treatment Comments:

·Narrative Report~

TOT Inspection Report Overall Narrative Comments: This is a single story - 4-bedroom home on a slab w/o basement. The original install permit in 2017 was for a 2-bedroom home. There is a water softener and a kitchen garbage disposal that the current owner does not use. The 1250 gal. concrete septic tank is very shallow with one corner actually at surface. I would recommend adding a 6" riser to each existing then add 6" of soil. The outlet Pipe is exiting the tank at a very steep angle causing the septic tank to back up into the inlet line. We will repair the steep outlet pipe the week of April 14th. The distribution box is a "plastic only" box in very good condition. There are no speed levelers, but the 2 header pipes are taking water equally. The two 100' rock and pipe soil absorption lines are 36" wide. There was no sewage surfacing or ponding and probing showed no saturation. The system accepted the 300 gal. water load test w/o any slowness or backing up.



GOVERNOR KIM REYNOLDS LT. GOVERNOR CHRIS COURNOYER

DIRECTOR KAYLA LYON

TIME OF TRANSFER INSPECTION TOT# 14677 ROGER GROTH CERT # 8813

Owner Name:

Allen & Sarah Detweiler

Address:

2834 285th St., Hopkinton, IA 52237

County:

Delaware

Inspection Date:


04/08/2025

Submitted Date:

4/12/2025

This page certifies a Time of Transfer inspection was conducted and submitted for the property listed above in accordance with Subrule 567 IAC 69.2(8).


4/12/2025 2:01:38 PM

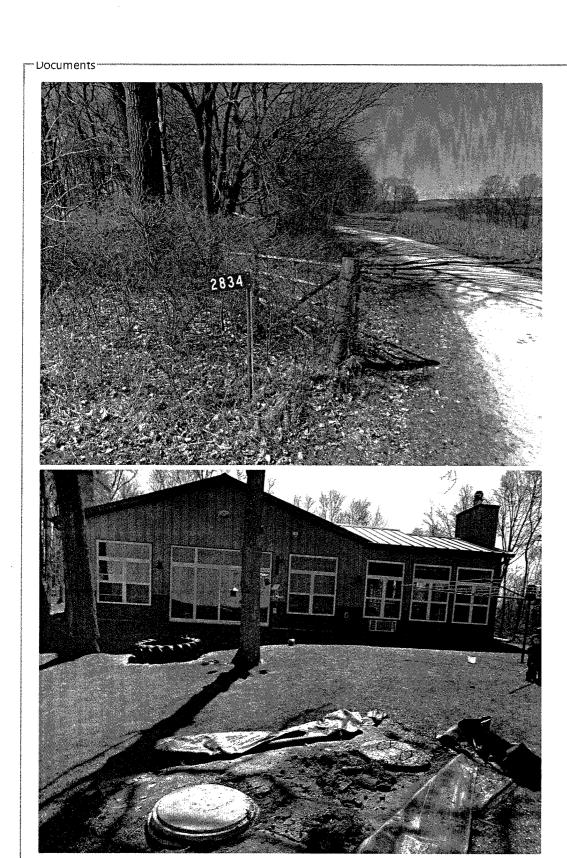










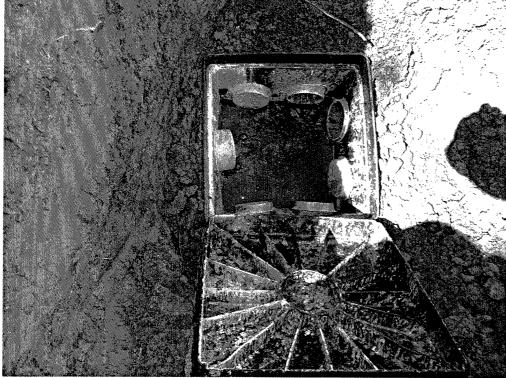

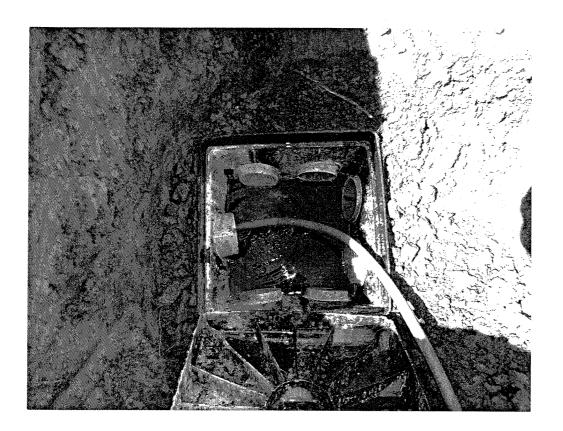

GROTH SERVICES



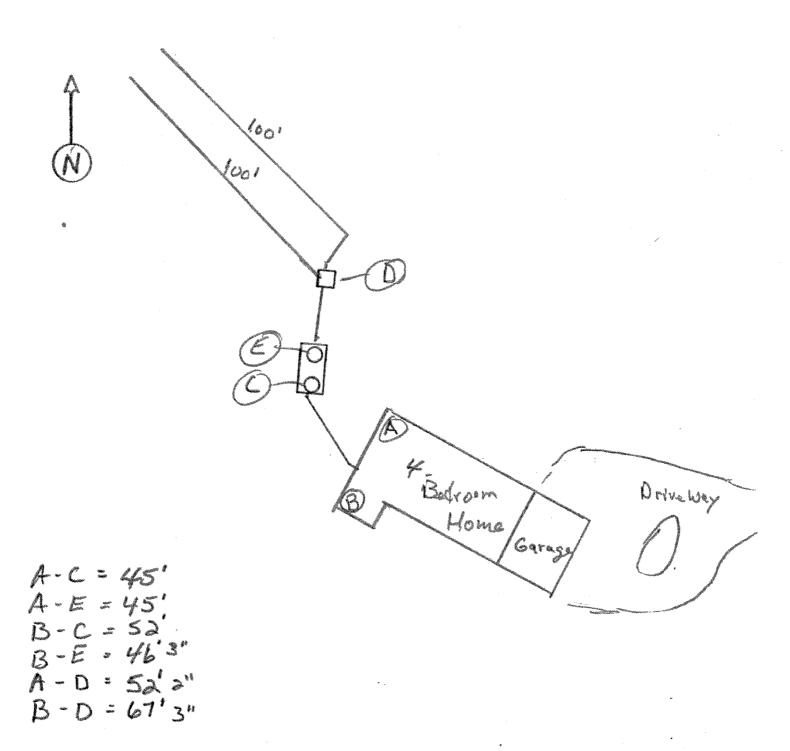

1250 gd, tank w/risus to surface 1-Esswent filter D-Box is 22" deep SAS IS rock & pipe
